Project Planning Phase

Project Planning Templa te(ProductBacklog,SprintPlanning, Stories, Story points)

Date	25 October 2026
Team ID	EN25CS3010534
Project Name	Global Olympic Sports Performance Analysis
Maximum Marks	8 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Use the below template to create product backlog and sprint schedule

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Data Management	USN-1	As a dashboard administrator, I can connect the four CSV datasets (athletes, medal results, games summary and all-time rankings) in Tableau using relationships on noc_code and year, so that every dashboard uses one unified data model.	5	High	Yashvi Agrawal
Sprint-1	Data Preparation	USN-2	As a data analyst, I can validate data types, regions and the medal efficiency formula, so that all KPIs and charts are accurate.	3	High	Yashvi Agrawal
Sprint-1	Global Performance Overview	USN-3	As a performance director, I can view KPI cards for athlete participation, sport categories entered and nations represented, so that I can assess overall participation at a glance.	3	High	Yashvi Agrawal
Sprint-1		USN-4	As a performance director, I can see total medals by nation on a world map, so that I can identify the leading countries.	5	High	Yashvi Agrawal

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-2	Trend Analysis	USN-5	As a performance director, I can see total medals awarded across the Games from 1992 to 2026, so that I can track how competition has changed over time.	3	Medium	Yashvi Agrawal
Sprint-2	Sport Category Analysis	USN-6	As a sports data analyst, I can compare average medals per athlete by sport category, so that I can find the strongest sports.	3	Medium	Yashvi Agrawal
Sprint-2	Country Performance	USN-7	As a performance director, I can compare countries by total, gold, silver or bronze medals using a KPI selector, so that I can benchmark nations by medal type.	5	High	Yashvi Agrawal
Sprint-2	Regional Efficiency	USN-8	As a sports funding officer, I can view regional KPI cards and average medal efficiency by region, so that I can see which regions win the most medals per athlete.	5	High	Yashvi Agrawal
Sprint-2		USN-9	As a sports funding officer, I can compare sports investment level with medal performance by country, so that I can judge the return on investment.	5	Medium	Yashvi Agrawal
Sprint-3	Host & Sport Distribution	USN-10	As a sports funding officer, I can compare medal totals across host countries and see the regional distribution by sport, so that I can understand host advantage and sport mix.	3	Medium	Yashvi Agrawal

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-3	Interaction & Filtering	USN-11	As a dashboard user, I can assemble and filter both dashboards by country, year, sport category, region and host country, so that I can focus on one segment across all charts.	8	High	Yashvi Agrawal
Sprint-3	Storytelling & Publishing	USN-12	As a viewer, I can follow a Tableau story and open the published dashboards in a Flask web app, so that I can explore the findings online.	8	High	Yashvi Agrawal

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	16	2 Days	29 Oct 2026	30 Oct 2026	16	30 Oct 2026
Sprint-2	21	2 Days	31 Oct 2026	01 Nov 2026	21	01 Nov 2026
Sprint-3	19	2 Days	02 Nov 2026	03 Nov 2026	19	03 Nov 2026
Total	56	6 Days	29 Oct 2026	03 Nov 2026	56	03 Nov 2026

Velocity:

Imaginewe have a 10-day sprint duration, and the velocity of the team is 20 (points per sprint). Let’s calculate the team’s average velocity (AV) per iteration unit (story points per day)


$$AV = \frac{sprint\ duration}{velocity} = \frac{20}{10} = 2$$

For this project the sprint duration is 2 days, and the team completed 16, 21 and 19 story points in the three sprints. Average velocity per sprint = (16 + 21 + 19) / 3 = 18.67 story points. Average velocity per day (AV) = velocity / sprint duration = 18.67 / 2 = 9.33 story points per day (56 story points in 6 days).

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time.

Prepared by: Yashvi Agrawal

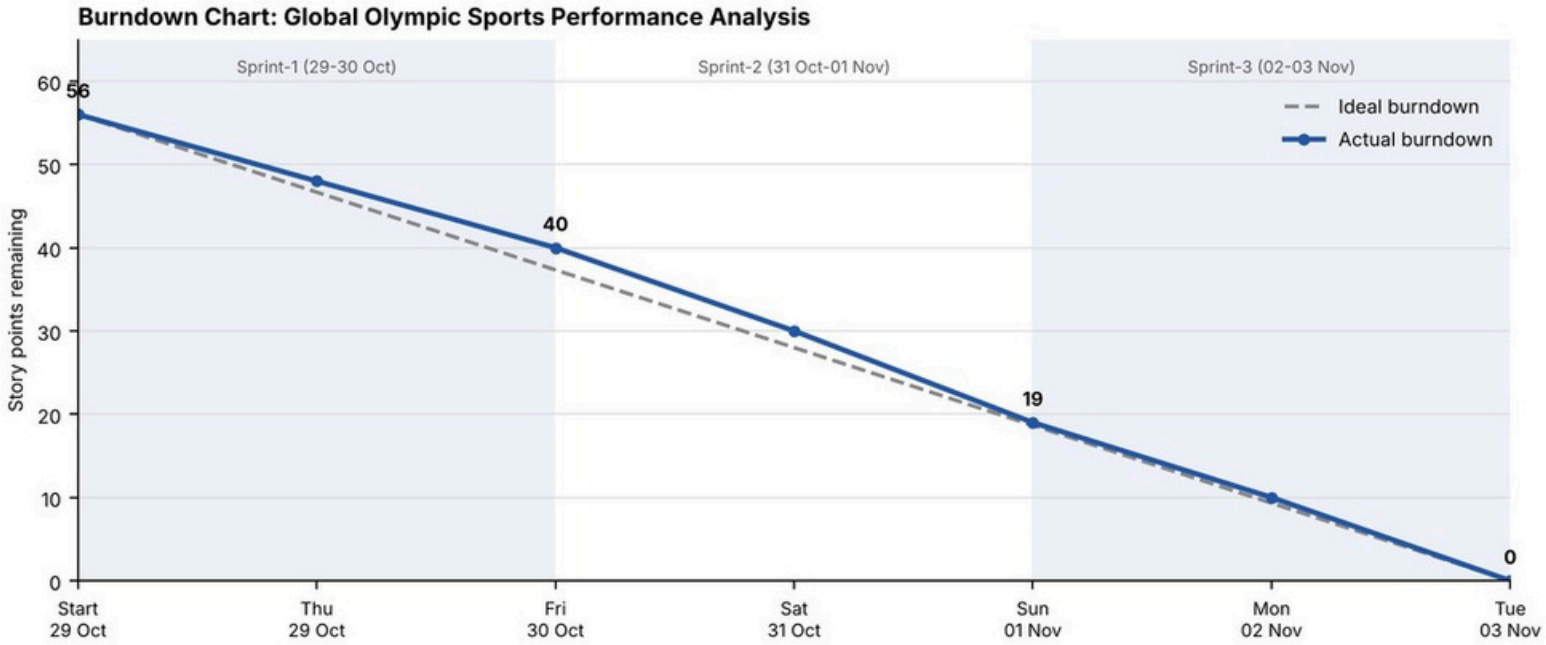

The team started with 56 story points on 29 Oct 2026 and burned them down to 0 by 03 Nov 2026. The actual line stayed within 1 to 3 points of the ideal line through the middle of the project and reached the ideal line by the end of Sprint-2, and all three sprints closed on their planned end dates (30 Oct, 01 Nov and 03 Nov 2026).

https://www.visual-paradigm.com/scrum/scrum-burndown-chart/
https://www.atlassian.com/agile/tutorials/burndown-charts

Reference:

https://www.atlassian.com/agile/project-management
https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software
https://www.atlassian.com/agile/tutorials/epics
https://www.atlassian.com/agile/tutorials/sprints
https://www.atlassian.com/agile/project-management/estimation
https://www.atlassian.com/agile/tutorials/burndown-charts
